


GANIT CHART

34	🔧	• Model-to-Vehicle Integration	12 days	Thu 2/11/27	Fri 2/26/27	
35	🔧	Connect camera feed to decision model	1 day	Thu 2/11/27	Thu 2/11/27	33,15
36	🔧	Map model decisions to vehicle commands	2 days	Thu 2/18/27	Fri 2/19/27	25,35
37	🔧	Test autonomous decision outputs	2 days	Mon 2/22/27	Tue 2/23/27	36
38	🔧	Debug model/control integration	3 days	Wed 2/24/27	Fri 2/26/27	37
39	🔧	• Autonomous Driving Testing	20 days	Wed 2/24/27	Tue 3/23/27	
40	🔧	Design controlled driving course	2 days	Wed 2/24/27	Thu 2/25/27	37
41	🔧	Perform low-speed autonomous tests	3 days	Mon 3/1/27	Wed 3/3/27	38,40
42	🔧	Analyze autonomous driving results	1 day	Thu 3/4/27	Thu 3/4/27	41
43	🔧	Improve model/control logic	3 days	Fri 3/5/27	Tue 3/9/27	42
44	🔧	Conduct additional driving trials	3 days	Wed 3/10/27	Fri 3/12/27	43
45	🔧	Test different conditions/scer	3 days	Mon 3/15/27	Wed 3/17/27	44
46	🔧	Analyze failures/erros	1 day	Thu 3/18/27	Thu 3/18/27	45
47	🔧	Make final performance improvements	3 days	Fri 3/19/27	Tue 3/23/27	46
48	🔧	• Vehicle Enclosure & Final Assembly	42 days	Thu 1/28/27	Fri 3/26/27	
49	🔧	Design electronics	4 days	Thu 1/28/27	Tue 2/2/27	14
50	🔧	3D print prototype mounts/case	2 days	Wed 2/3/27	Thu 2/4/27	49
51	🔧	Test component fit	1 day	Fri 2/5/27	Fri 2/5/27	50
52	🔧	Revise enclosure/mou	2 days	Mon 2/8/27	Tue 2/9/27	51
53	🔧	Print final enclosure/mou	1 day	Wed 2/10/27	Wed 2/10/27	52
54	🔧	Install final enclosure/mou	2 days	Wed 3/24/27	Thu 3/25/27	47,53
55	🔧	Cable management/fi hardware	1 day	Fri 3/26/27	Fri 3/26/27	54
56	🔧	• Final Autonomous System Testing	8 days	Mon 3/29/27	Wed 4/7/27	
57	🔧	Full autonomous system test	2 days	Mon 3/29/27	Tue 3/30/27	55
58	🔧	Reliability/repe testing	3 days	Wed 3/31/27	Fri 4/2/27	57
59	🔧	Fix final issues	2 days	Mon 4/5/27	Tue 4/6/27	58
60	🔧	Final autonomous driving verification	1 day	Wed 4/7/27	Wed 4/7/27	59
61	🔧	• Documentation & Final Demonstration	7 days	Thu 4/8/27	Fri 4/16/27	
62	🔧	Document hardware/PCB system	2 days	Thu 4/8/27	Fri 4/9/27	60
63	🔧	Document model/software system	2 days	Thu 4/8/27	Fri 4/9/27	60
64	🔧	Document testing/results	2 days	Thu 4/8/27	Fri 4/9/27	60
65	🔧	Complete final report	3 days	Mon 4/12/27	Wed 4/14/27	62,63,64

GANIT CHART

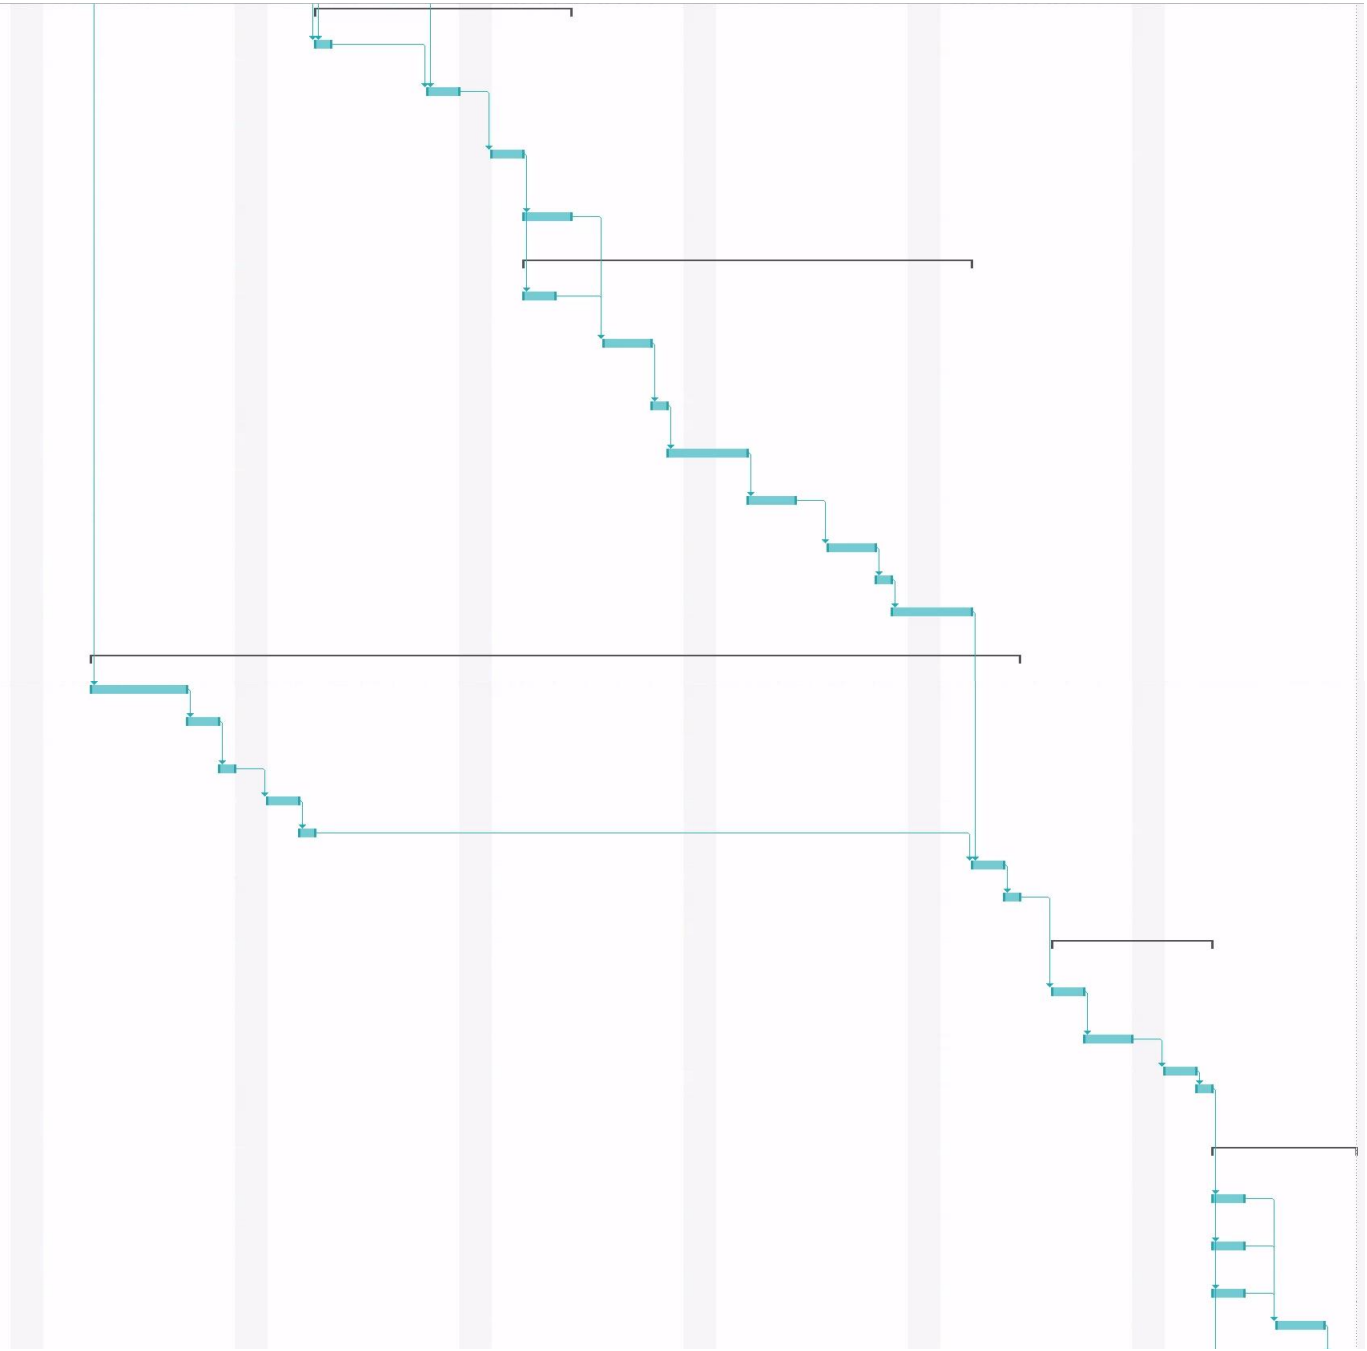

66		Prepare presentation	1 day	Thu 4/15/27	Thu 4/15/27	65
67		Prepare autonomous demonstration course	2 days	Thu 4/8/27	Fri 4/9/27	60
68		Practice final demonstration	1 day	Fri 4/16/27	Fri 4/16/27	66,67

